ebXML Transport, Routing and Packaging Team -- Work Plan

Activity Name	Start Date	Finish Date
Messaging Service v0.8...	8/10/00	
Reliable Messaging Spec (Fujitsu)		
Update, TRP approves v0.80	8/7/00	10/5/00
Update, TRP approves v0.84	10/6/00	11/2/00
Update for integration	11/13/00	12/22/00
Security Appendix (MH)		
Draft v0.1 available for TRP	11/17/00	
TRP comment on draft v0.1	11/20/00	12/1/00
Prepare draft v0.2 (payload)	12/4/00	12/22/00
Prepare draft v0.3 (headers)	1/8/01	1/12/01
TRP comment on Draft v0.3	1/15/01	1/26/01
Service Interface/MSH Query (CF)		
Prepare Draft v0.1	11/20/00	12/1/00
TRP Comment on Draft v0.1	12/4/00	12/15/00
Prepare draft v0.2	12/18/00	12/22/00
Messaging Service v1.0 (IMR)		
Address outstanding comments	11/9/00	12/22/00
Edit in new sections	1/8/01	1/26/01
Release to POC for Vancouver	1/15/01	
TRP Prepares Final Draft	1/29/01	2/9/01
Release to POC for XML1	2/12/01	
Quality Review	2/12/01	2/16/01
ebXML Member Review	2/19/01	3/2/01
Final TRP Cleanup	3/5/01	3/23/01

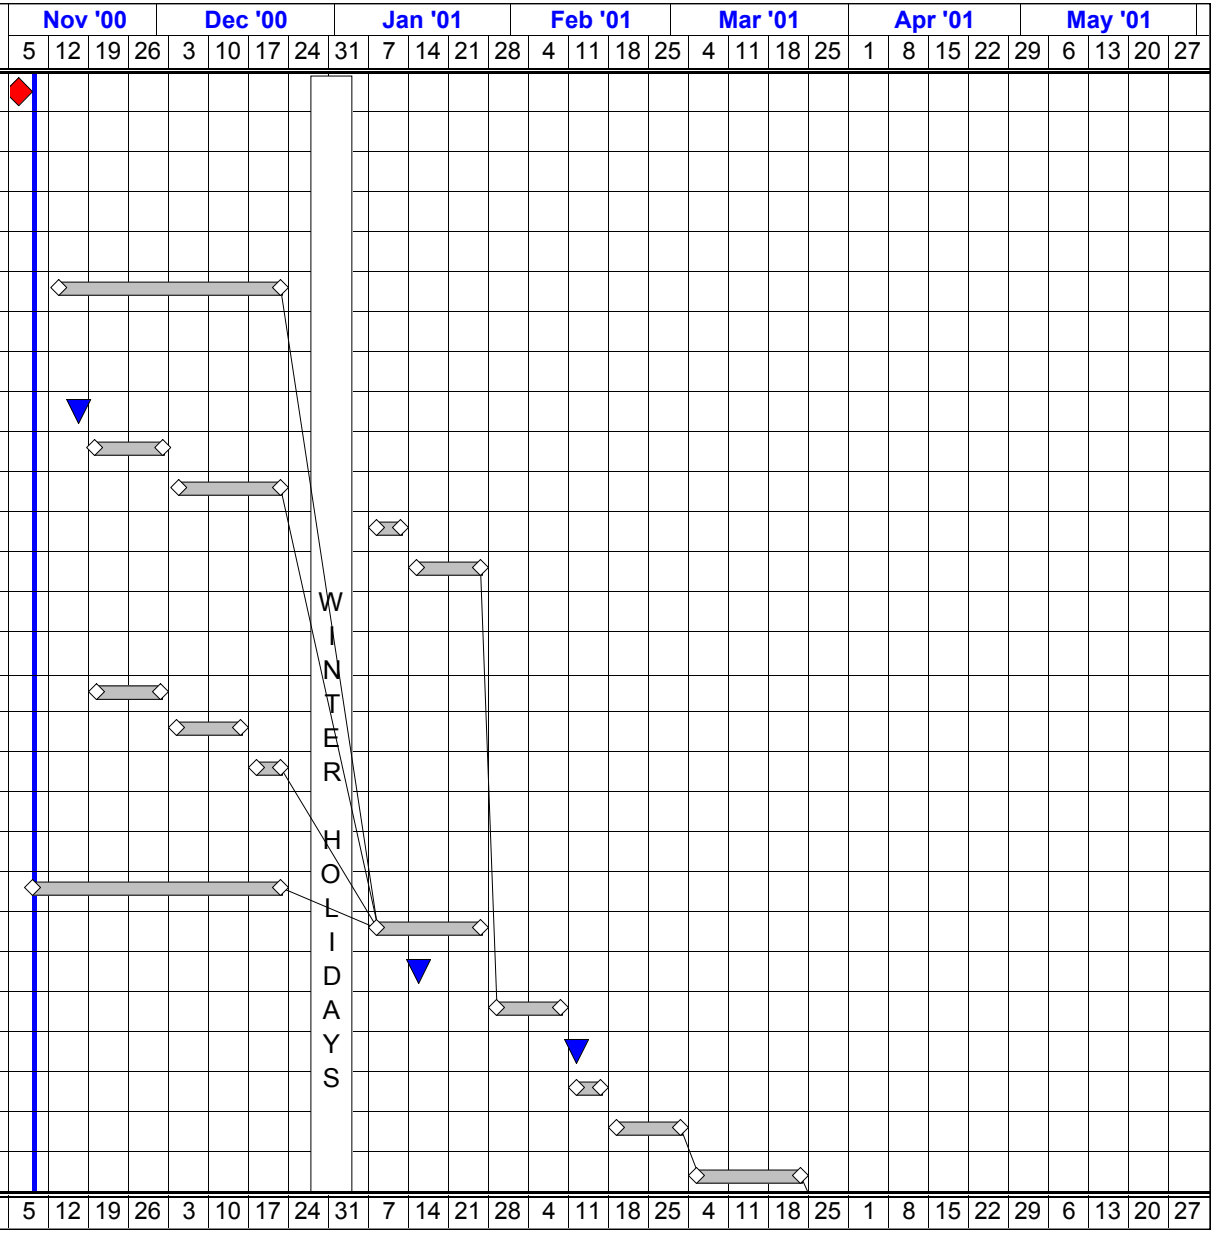

ebXML Transport, Routing and Packaging Team -- Work Plan
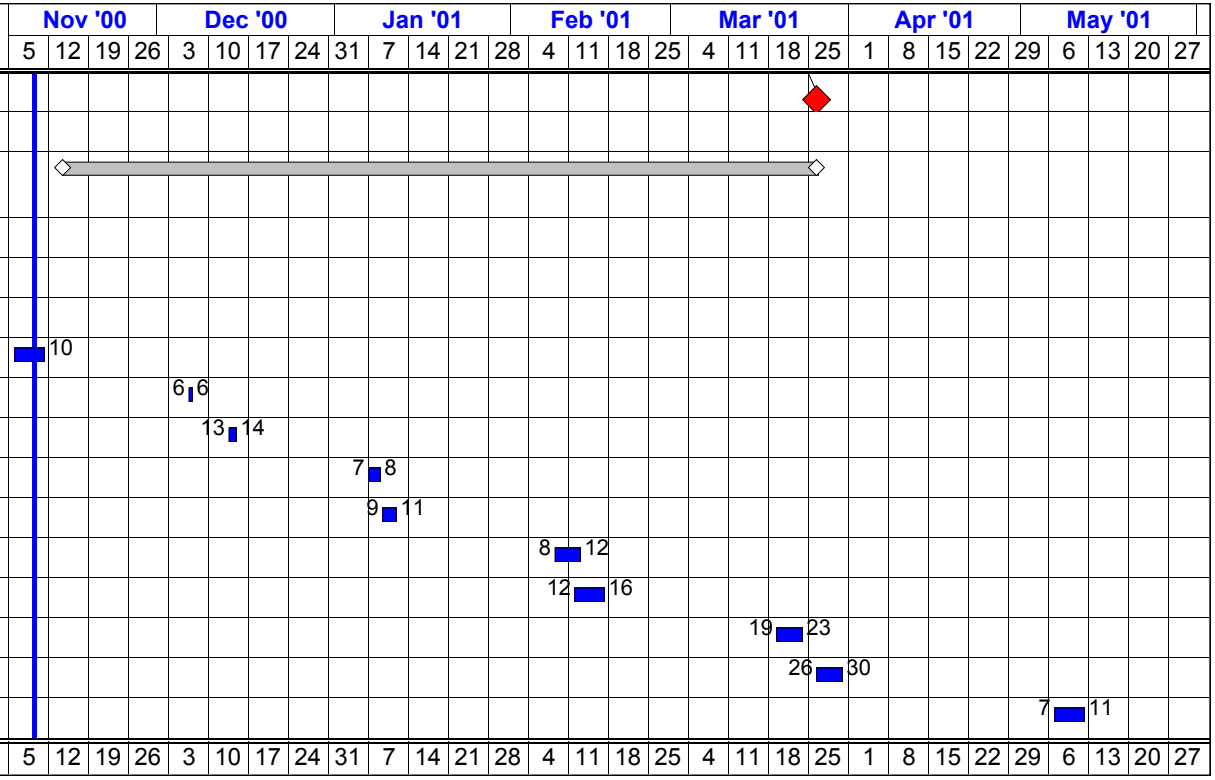
Activity Name	Start Date	Finish Date
Approve v1.0 at Geneva	3/26/01	
Complete Final Req Document (DBu)	11/14/00	3/26/01
ebXMLSan Jose Meeting	8/7/00	8/11/00
TRP F2F, Dallas	9/26/00	9/28/00
ebXMLTokyo Plenary	11/6/00	11/10/00
ebXML Security F2F, Boston	12/6/00	12/6/00
W3C-XP, Redmond	12/13/00	12/14/00
Small Edit Meeting, UK	1/7/01	1/8/01
TRP F2F, UK	1/9/01	1/11/01
Small Edit Meeting, ~Seattle?	2/8/01	2/12/01
ebXML Vancouver Plenary	2/12/01	2/16/01
XML1, London	3/19/01	3/23/01
ebXML Geneva Plenary	3/26/01	3/30/01
ebXML Vienna Plenary	5/7/01	5/11/01
